


PROJECT MANAGEMENT PLAYBOOK

CREATE A PROJECT PLAN

Build a project plan

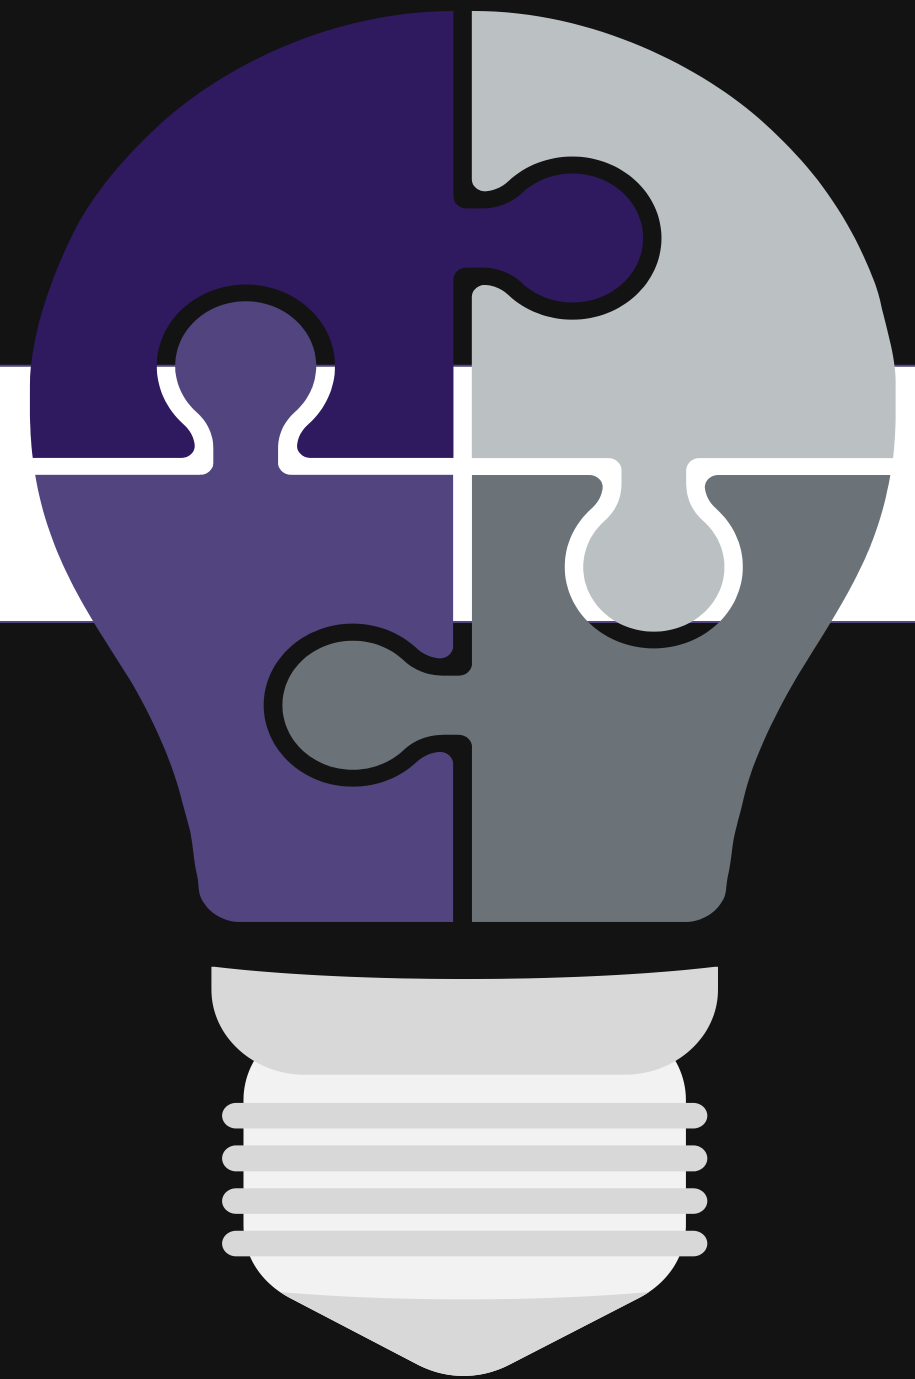

INSTRUCTIONS: Introduction and background

For this playbook, you'll take the role of project manager to lead the initiative to revamp Moodies' customer service portal. The goal is to enhance customer self-service and reduce the current dependency on direct customer service interactions. This update is critical for scaling support to match the growing demand for our mood-responsive shoes. **You'll be creating a project plan for the initiative.** Senior management wants to **kick off the project at the beginning of the year (Jan 2).**

Moodies is at the forefront of innovative footwear, offering unique shoes that change color based on the wearer's mood. With two main product lines for kids and adults, our popularity has surged, leading to a high volume of customer inquiries. Our current support system, relying heavily on FAQ and direct email communication, is no longer sustainable. Leadership has identified the need for a more efficient, user-friendly customer support experience. This project will focus on redesigning the customer support portal to provide quick, efficient service while maintaining the personalized touch that Moodies is known for.

REVIEW: Gathering information

You have been provided with the initial milestones for Moodie's newest customer improvement initiative. Your task is to develop a project plan that aligns with the milestones using the provided template. Below is a list of the five milestones.

1. Identifying and writing new content
2. Designing a page for new content
3. Implementing content on the website
4. Testing and quality assurance
5. Enablement for customer service representatives

Building the project plan requires breaking down the work into smaller, more understandable tasks, and estimating how long they will take. This generally requires reaching out to stakeholders for more information.

Use the information from the document linked below to fill out the information in the project plan on the next slide. **For dependencies, assume the project's tasks are done sequentially.**

[Module 4 Playbook – Email Communication](#)

COMPLETE: Create the project plan

Break each milestone into **at least two tasks** (there could be more!) and then fill in the additional columns.

Assumptions used:

- Working days are from monday to friday
- All tasks are sequential
- 1 week = 5 working days.
- Half week = 3 working days.

Note :

Project start date is mentioned as January 2, 2027. since it is saturday, i would consider January 4th 2027 as project start date.

COMPLETE: Create the project plan

Milestone #	Task #	Task Description	Duration	Start Date	Finish Date	Dependencies
1	1.1	Content analysis	1 week	Jan 4, 2027	Jan 8, 2027	None
1	1.2	Content research and gathering	1.5 weeks	Jan 11, 2027	Jan 20, 2027	1.1
1	1.3	Content writing and review	3 weeks	Jan 21, 2027	Feb 10, 2027	1.2
2	2.1	Page design planning	1 week	Feb 11, 2027	Feb 17, 2027	1.3
2	2.2	Page layout and graphic design	2 weeks	Feb 18, 2027	Mar 3, 2027	2.1
2	2.3	Content integration into page (prototype)	1.5 weeks	Mar 4, 2027	Mar 15, 2027	2.2
3	3.1	Technical integration planning	1 week	Mar 16, 2027	Mar 22, 2027	2.3
3	3.2	Content implementation on website	2.5 weeks	Mar 23, 2027	Apr 8, 2027	3.1
4	4.1	QA test planning & test case creation	1.5 weeks	Apr 9, 2027	Apr 20, 2027	3.2
4	4.2	QA testing and issue reporting	2 weeks	Apr 21, 2027	May 4, 2027	4.1
4	4.3	User acceptance testing (UAT)	2 weeks	May 5, 2027	May 18, 2027	4.2
5	5.1	Customer service representative training	2 weeks	May 19, 2027	Jun 1, 2027	4.3
5	5.2	Enablement and integration planning	1 week	Jun 2, 2027	Jun 8, 2027	5.1
5	5.3	Phased rollout	2 weeks	Jun 9, 2027	Jun 22, 2027	5.2


REVIEW: Breaking the work down further

Now that you've put together the project plan, you begin working with the head of customer service to break down the work for the first milestone into more detail. Below is what you came up with. Use this list of tasks below to create a project network diagram on the following slide. Then, determine the critical path and calculate the shortest amount of time it would take to complete this milestone.

Task #	Task Description	Duration	Dependencies
1.1.1	Analyze customer satisfaction data	3	–
1.1.2	Review existing content	5	–
1.2.1	Identify frequently asked questions	5	1.1.1, 1.1.2
1.2.2	Team ideation sprint	2	1.1.1
1.2.3	Prepare report	7	1.2.1, 1.2.2
1.3.1	Define content structure	5	–
1.3.2	Create content drafts	10	1.2.3, 1.3.1
1.3.3	Review, revise, and finalize content	10	1.3.2

COMPLETE: Create a project network diagram

Use the list of tasks on the previous slide to create a network diagram. Then, highlight the critical path and calculate the shortest time to complete the milestone. **Tip:** use elbow connectors to link the tasks. You can copy and paste the one below. The task numbers and durations (in parentheses) have already been added to the slide. Drag and drop to move them.

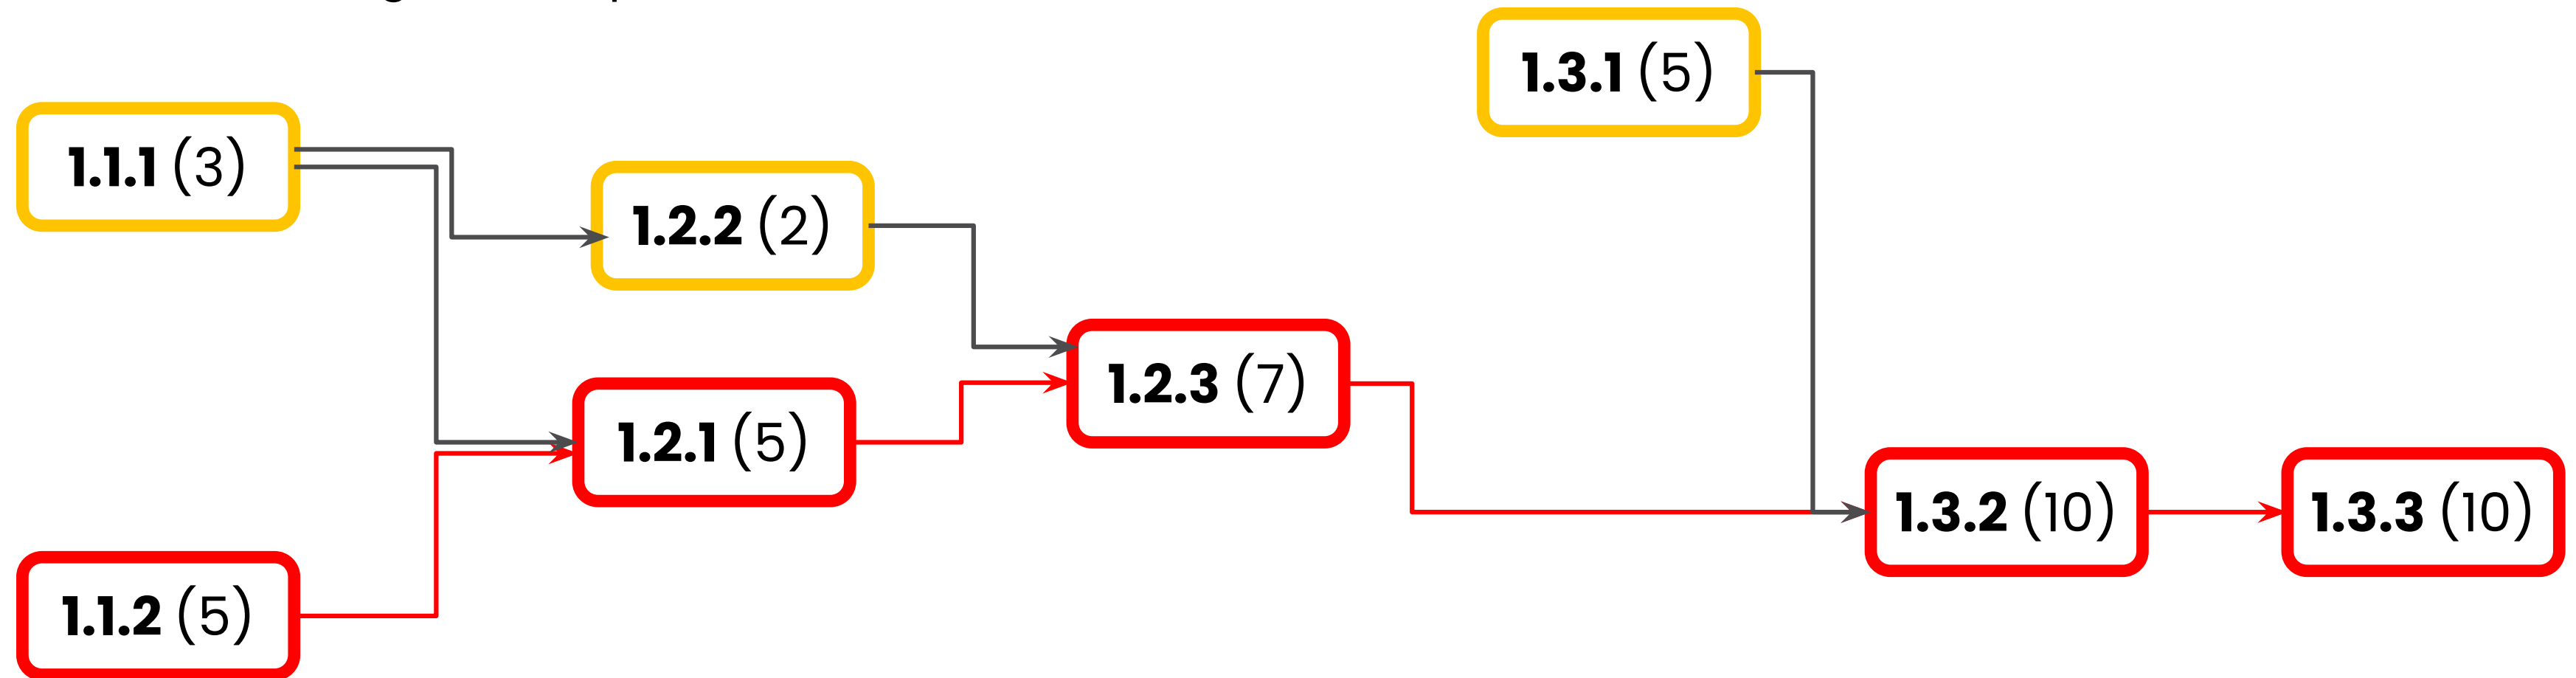

Minimum time to complete the milestone: 37
