


PROJECT MANAGEMENT PLAYBOOK

MANAGE RISKS

**Create a risk
management plan**

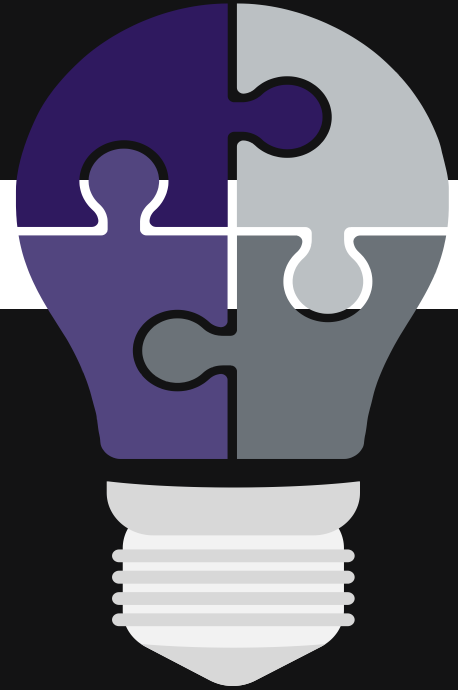

COMPLETE: Potential areas of risk

PROMPT/QUESTION	RESPONSE
Based on the project playbook scenario in the previous slides, identify at least three to four general potential issue areas of risk.	I identified following as potential risks for moodies, 1. Content Development and Availability – The Content Author planned absence could delay content analysis, writing, and review. 2. QA and Testing Capacity – The QA Tester departure could create a resource gap during testing and UAT. 3. Technical Integration and Implementation – Technical integration and website implementation activities could require rework and affect subsequent milestones. 4. Content Relevance and Coverage – If new content does not adequately address high-volume customer questions, the project may not achieve its customer service and workload-reduction objectives.

COMPLETE: Potential areas of risk

Do the project objectives lead to the company/project goal? Why or why not?

Yes.

The project objectives directly support Moodies' goal by **addressing high-volume customer queries, reducing support workload and turnaround time, and improving customer satisfaction and retention.**

- **20% increase in customer satisfaction** → improves customer experience and supports retention.
- **40% reduction in representative response time** → helps handle high-volume queries more efficiently.
- **80% reduction in social media questions** → encourages customers to use the self-service portal.
- **Resolution time reduced from 4 to 2 days** → lowers turnaround time and improves service efficiency.

These objectives create value by making customer support faster, more efficient, and more responsive, supporting both customer satisfaction and retention.

COMPLETE: Risk assessment

Perform a risk assessment based on **the project plan** portion of the [project scenario](#). Identify any potential team related risks and then identify 4-6 potential risks to the project plan (milestones and tasks).

PROMPT/QUESTION	RESPONSE
From the list of team members, identify any missing roles and other areas of potential risk .	Following are missing roles and other areas of potential risks • Backup Content Author: Planned absence could delay content research, writing, and review. • Replacement QA Tester: QA tester departure creates a gap in testing and UAT. • Business/Requirements Analyst: No dedicated role for analyzing high-volume customer questions and defining content requirements. • Training/Change Support: No dedicated resource for employee training and adoption during rollout. • Knowledge Transfer: QA tester departure could result in loss of project knowledge. • Resource Bottlenecks: Limited engineering/design resources could cause delays if rework is required.

COMPLETE: Risk assessment

Project plan/Milestones assessment

Identify 4-6 potential risks to the project plan.

Key Risk: Resource availability is the significant concern because the Content Author is taking time off and the QA Tester is leaving, potentially creating delays across multiple milestones.

Below table represents potential risks across each milestones.

Risk	Affected Tasks
1. Content Author Unavailability	M1: T1–T3
2. QA Tester Departure	M4: T9–T11
3. Technical Integration Issues	M3: T6–T8
4. Design Delays / Rework	M2: T4–T5
5. Insufficient Coverage of High Volume Questions	M1 & M4: T1–T3, T9–T11
6. Training & Rollout Delays	M5: T12–T14

COMPLETE: Determine risk probability and impact

Fill in the table with each risk and then determine the probability and potential risk impact (high, medium, low) of each risk. There's a wide range of acceptable answers. You can use the list at the bottom of the [playbook scenario document](#) to give you some ideas.

Risk description	Probability (high, medium, low)	Impact (high, medium, low)
1. Content Author Unavailability: Planned time off may delay content analysis, research, writing, and review.	High	High
2. QA Tester Departure: The QA tester departure may leave insufficient resources for QA testing, issue reporting, and UAT.	High	High
3. Technical Integration Issues: Problems during website content integration or technical implementation may require rework and delay the project.	Medium	High
4. Design Delays / Rework: Changes or delays in page planning and design may postpone content implementation.	Medium	Medium
5. Insufficient Coverage of High-Volume Questions: New content may not fully address the most frequent customer questions, requiring revisions and additional testing.	Medium	High
6. Training & Rollout Delays: Delays in customer service representative training or enablement may affect adoption and the final rollout.	Medium	Medium

REVIEW: Unforeseen risk – Curveball scenario

You were just notified by the legal team for Moodies that California, New York, Texas, Arizona, Colorado, and Florida just passed laws requiring all commerce websites to be available in both English and Spanish effective March of the upcoming year. At present, the content written for the new customer support portal is only written in English. Your task is to develop a risk mitigation plan and an email communicating the plan and update frequency.

Do your best to identify the risk mitigation strategy and tasks to address this situation, along with a reasonable timeline. Your best estimates are fine.

>> Continue on the next slide

COMPLETE: Unforeseen risk – Curveball scenario

Complete the table below by selecting a risk management strategy and populating tasks, descriptions, and timelines for your plan.

Question	Answer
Which risk management strategy will you use in this scenario? <i>(Avoidance, mitigation, transfer, or acceptance)</i> 💡 <i>Hint: Reflect on whether this risk should be addressed internally or through outside expertise.</i>	Transfer – Outsource Spanish translation to a qualified translation vendor to reduce internal resource constraints and ensure bilingual content is completed before the March compliance deadline.

Key point: The vendor handles the translation, while Moodies retains responsibility for review, approval, compliance, implementation, and testing.

COMPLETE: Unforeseen risk – Curveball scenario

Task	Description	Timeline
Confirm Legal Requirements	Confirm bilingual requirements and March compliance deadline with Legal.	Week 1
Assess Translation Scope & Cost	Identify content requiring translation and obtain vendor estimates.	Week 1–2
Check Contingency Budget	Confirm whether available contingency funds cover the estimated translation cost.	Week 2
Raise Change Request if Needed	Request additional funding approval if the contingency budget is insufficient.	Week 2–3
Select Translation Vendor	Engage a qualified vendor after funding approval.	Week 3
Outsource Translation	Provide finalized English content to the vendor for Spanish translation.	Weeks 4–7
Review & Approve Translation	Content and Legal teams review the translated content.	Weeks 8–9
Implement & Test	Add Spanish content and test the bilingual portal.	Weeks 10–11
Final Compliance Review	Legal confirms compliance and readiness before the March deadline.	Week 12

COMPLETE: Develop a risk communication plan

PROMPT/QUESTION	RESPONSE
Write an email to stakeholders describing your risk mitigation plan, status, and expected meeting frequency for updates. <i><Subject Line: keep it concise and informative></i> <i><Briefly state the purpose of the email></i> <i><Clearly describe the risk(s) the project is facing and the impact></i> <i><Briefly explain the risk mitigation plan to address the risks></i> <i><Set expectations on when stakeholders should expect updates></i> <i><Close the email by soliciting questions and feedback></i>	Please check next slide for email draft



Try writing the email independently first, then ask your favorite AI tool to review your work and suggest improvements. Remember to give AI all of the context it needs to write a clean, effective email. (Optional)

COMPLETE: Develop a risk communication plan

Subject: Moodies Portal – Spanish Translation Compliance Risk & Action Plan

Dear Stakeholders,

The purpose of this email is to provide an update on the new Spanish-language website requirement and our response plan.

Risk: New laws require commerce websites in CA, NY, TX, AZ, CO, and FL to support both English and Spanish by March. Our current portal content is English only, creating a potential compliance and timeline risk.

Plan: We will outsource Spanish translation to a qualified vendor using available contingency funds. If the vendor cost exceeds the available contingency budget, we will submit a change request for additional funding and approval before proceeding.

The vendor will handle the translation, while Moodies retains responsibility for review, approval, compliance, implementation, and testing.

Updates: Stakeholders will receive weekly updates on translation progress, budget usage, timeline, and risks. Any issue affecting the March compliance deadline or requiring a change request will be communicated immediately.

Please share any questions, concerns, or feedback regarding this plan.

Best regards,
Radha Manjunath
Project Manager
