


PROJECT MANAGEMENT PLAYBOOK

MONITOR PROGRESS AND CONTROL QUALITY

Develop a project
status report

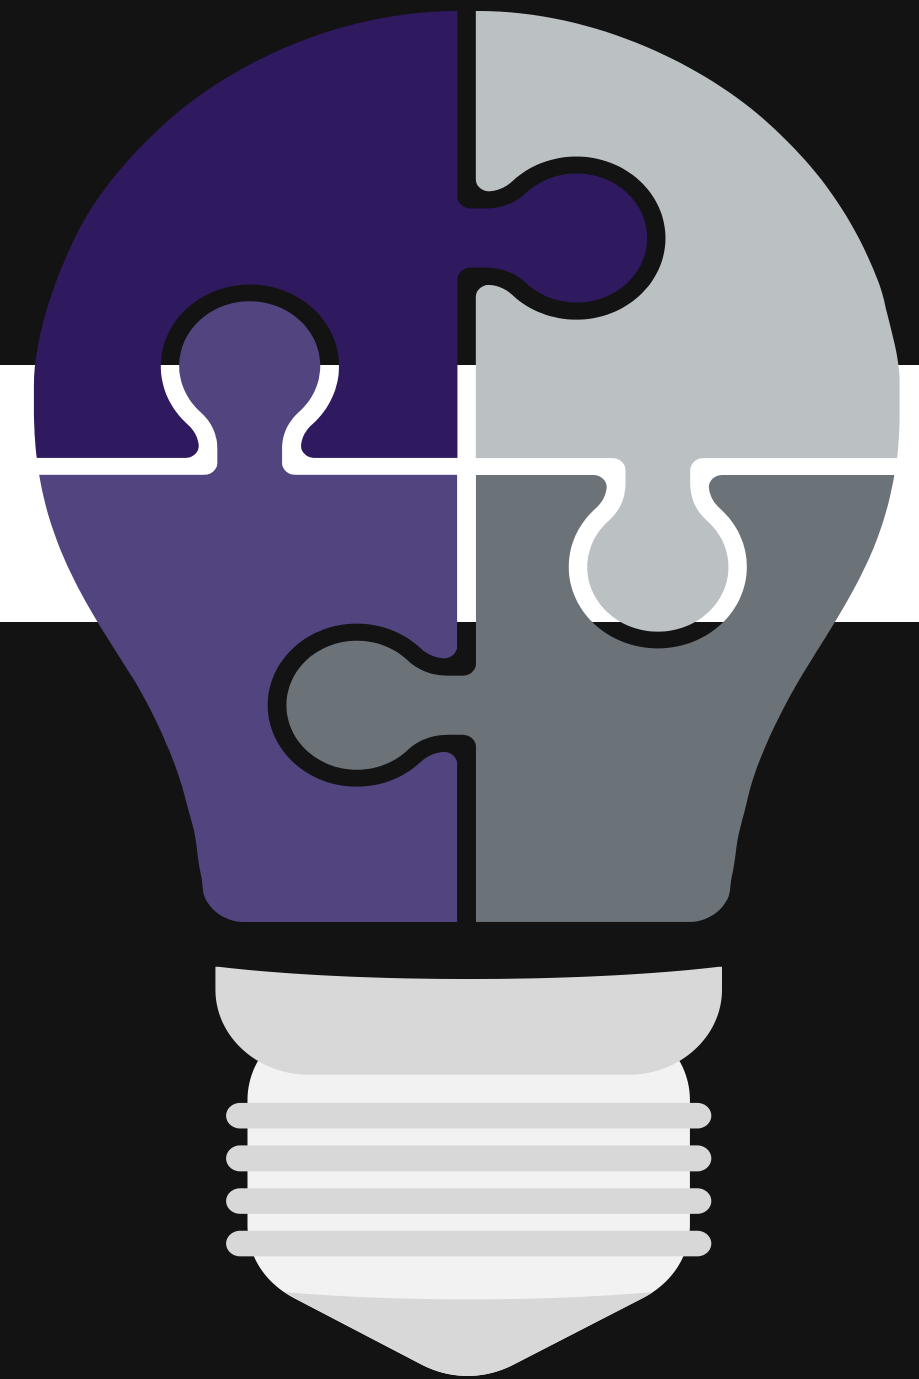

COMPLETE: Identify the types of information to share

What level of information is important to each group? List at least one example for each. Review the [PROJECT PLAN](#) here.

	NAME AND TITLE	INFORMATION & EXAMPLE Provide the level of information: (High, very detailed, etc.) and an example.
Project team	Diana Delaney , Software Engineer Stu Sampson , Quality Engineer Andy Adler , Content Creator Rika Rickles , Chatbot Rep. Hans Hindleman , Product Designer Naomi Brown , Customer Service Lead	Detailed, task level information. Include task status, dependencies, blockers, upcoming activities, and actions needed. Example: The chatbot scenarios are blocked due to resource/skill constraints. Diana and Rika need to coordinate on the technical requirements and next steps.
People managers	engineering@moodies.com design@moodies.com content@moodies.com	Summary level information focused on team capacity, resource issues, and escalations. Example: Product design is behind schedule because of an unexpected absence, which may affect dependent activities. A resource adjustment may be needed to recover the schedule.
Executive leadership	Bernard Bentley , Chief Financial Officer Melinda Carlyle , Head of Customer Experience	High level, strategic information focused on overall project health, major risks, budget, schedule, and decisions needed. Example: Delays in design and chatbot development may put the planned launch date at risk. Leadership approval may also be required for additional content budget.

COMPLETE: Project health snapshot

	Overall project health	Progress towards completion	Project due date	Weeks until launch
PROMPT/ QUESTION	Is your project at green, yellow or red?	Calculate the amount of work that has been completed.	When is this project scheduled to be completed (ie what's the due date)?	How many weeks does the project team have to complete the remaining work?
RESPONSE	RED – At Risk: 41.18% of project activities are complete, with 1 task overdue and 2 tasks blocked. Several critical activities, including QA, customer training, soft launch, and final launch, have not yet started. Immediate action is needed to address blockers and protect the April 8 launch date.	41.18%	Apr 08	4 weeks

COMPLETE: Evaluation and explanation


PROMPT/QUESTION	RESPONSE
Explain your reasoning. What factors went into determining the overall health of this project? Be sure to include: • The formula you would use to calculate progress towards completion. • What specific pieces of information in the project plan make you confident in your assessment of the health risk? List at least two.	Formula used to calculate progress is Progress % = (Number of completed activities ÷ Total number of activities) × 100 = (7 ÷ 17) × 100 = 41.18% Factors supporting the RED health assessment: 1. Schedule risk: Only 41.18% of activities are complete, while 5 activities (29.41%) have not started and the project has only 4 weeks until the April 8 launch. 2. Blocked and overdue work: 1 activity is overdue (product design templates) and 2 activities are blocked, including the creation of 16 chatbot FAQ scenarios. These delays can affect dependent activities. 3. Critical downstream activities: QA testing, customer training, internal soft launch, and final product launch have not started, leaving limited time to complete and test the remaining work. Overall assessment: The combination of low completion, blocked/overdue activities, and limited time remaining makes the project RED – At Risk and requires immediate action to protect the April 8 launch date.

COMPLETE: Project & status orientation

PROMPT/QUESTION	RESPONSE
Create your email introduction. Address the following: ● Why might someone be on the mailing list for this project? ● What are the agreed upon goals for this project? List at least two. ● Where can people receiving this email find more information? <i>Feel free to reference the Mentors R Us project status report example as you complete the next slides.</i>	Subject: Weekly Project Update – Moodie’s Customer Support Redesign Hello everyone, You are receiving this email because you are part of the Moodie’s project team, leadership team, or stakeholder group involved in the Moodies Customer Support Redesign project. This update provides a snapshot of project progress, health, current risks, and actions needed. As a reminder, the agreed upon goals of this project are to: ● Increase customer satisfaction by 20%. ● Reduce customer service representatives’ time spent on inquiries by 40%. ● Reduce customer questions through social media by 80%. For more information on project tasks, timelines, owners, and status, please review the Moodies Project Plan . If you have any questions, need more information, or have feedback on this update, please don’t hesitate to reach out to me directly. Best, Radha Manjunath Project Manager

COMPLETE: Provide a quick synopsis

PROMPT/QUESTION	RESPONSE
Based on the project plan, what information is absolutely critical for everyone to know? Create a TL;DR in the same style of the status report. Provide a headline and then include the following: • Are there any concerns that people should be aware of? • If so, how are you/your project team planning to address them? • Are there any immediate action items for anyone outside the project team?	TL;DR – Project is at risk of schedule delays; immediate attention is needed to address blocked work and protect the April 8 launch. The team is currently 41.18% complete. Product design templates are overdue, which has blocked FAQ development. In addition, creation of the 16 chatbot scenarios is blocked due to skill and time constraints. These delays may affect downstream activities, including QA, customer training, and the planned launch. How we are addressing the concerns: • The team is prioritizing the remaining design work and completing content ingestion as pages are received. • The team is evaluating options for completing the chatbot scenarios, with contracting external support as the preferred option. • The project team will continue monitoring the schedule and dependencies closely to protect the April 8 launch. Immediate action outside the project team: • Leadership approval is needed for the additional budget allocation required to contract out new content creation and potentially support chatbot scenario development.



Check your work with AI. Share your email introduction with your favorite AI tool, then ask for a curated TL;DR. How does it compare to what you authored? (Optional)

COMPLETE: Share insights & recommendations

PROMPT/QUESTION	RESPONSE
Based on the information you’ve captured on the project plan, your knowledge as a project manager, and the assessed health risk, provide at least two insights and two recommendations. Remember that effective insights and recommendations provide a meaningful and unique perspective for your stakeholders, and demonstrates your expertise as a project leader.	Based on the project plan and the RED – At Risk assessment, I would use these: Insight 1: The overdue product design templates are creating a cascading schedule risk because FAQ development depends on those templates. With only four weeks remaining before launch, additional delays could affect QA, training, and launch activities. Recommendation 1: Prioritize the remaining design templates and coordinate closely with Content to begin FAQ development immediately as templates become available. Insight 2: The chatbot work has a resource and skills constraint, making it difficult for the current team to complete all 16 scenarios within the timeline. Recommendation 2: Obtain approval for external support to complete the chatbot scenarios. If additional support cannot be secured quickly, consider launching with fewer scenarios and adding the remaining scenarios incrementally.

COMPLETE: Action items & next steps

PROMPT/QUESTION	RESPONSE
List at least three action steps for the project team and/or relevant stakeholders. Be sure to Include: • Who owns the action item • When it's due • What will be accomplished or delivered once the action item is done • If there will be follow up from you and when	1. Complete Product Design Templates Owner: Hans Hindleman Due: Mar 10 Action Item : Complete remaining templates to unblock FAQ development. PM follow-up: Mar 11 2. Resolve Chatbot Resource Constraints Owner: Rika Rickles + PM Due: Mar 11 Action Item : Confirm approach for completing 16 chatbot scenarios. PM follow-up:Mar 12 3. Approve Additional Budget Owner: Leadership / Project Sponsor Due: Mar 12 Action Item : Approve funding for contracted content/support. PM follow-up: Mar 13. Note : Due dates were set based on March 8 as the reporting date, with 4 weeks remaining until the April 8 launch.
